


EROSION CONTROL PLANS

Builders and Owners in the City of Fairview:

When submitting your erosion control plan, please include the following:

1. Building footprint and setbacks from the property line;
2. Public easements and right-of-ways with dimensions;
3. Silt fencing, particularly around areas bordering riparian zones;
4. Runoff direction.

If you have any questions regarding these requirements, please call the
Public Works Department at (503) 674-6206.

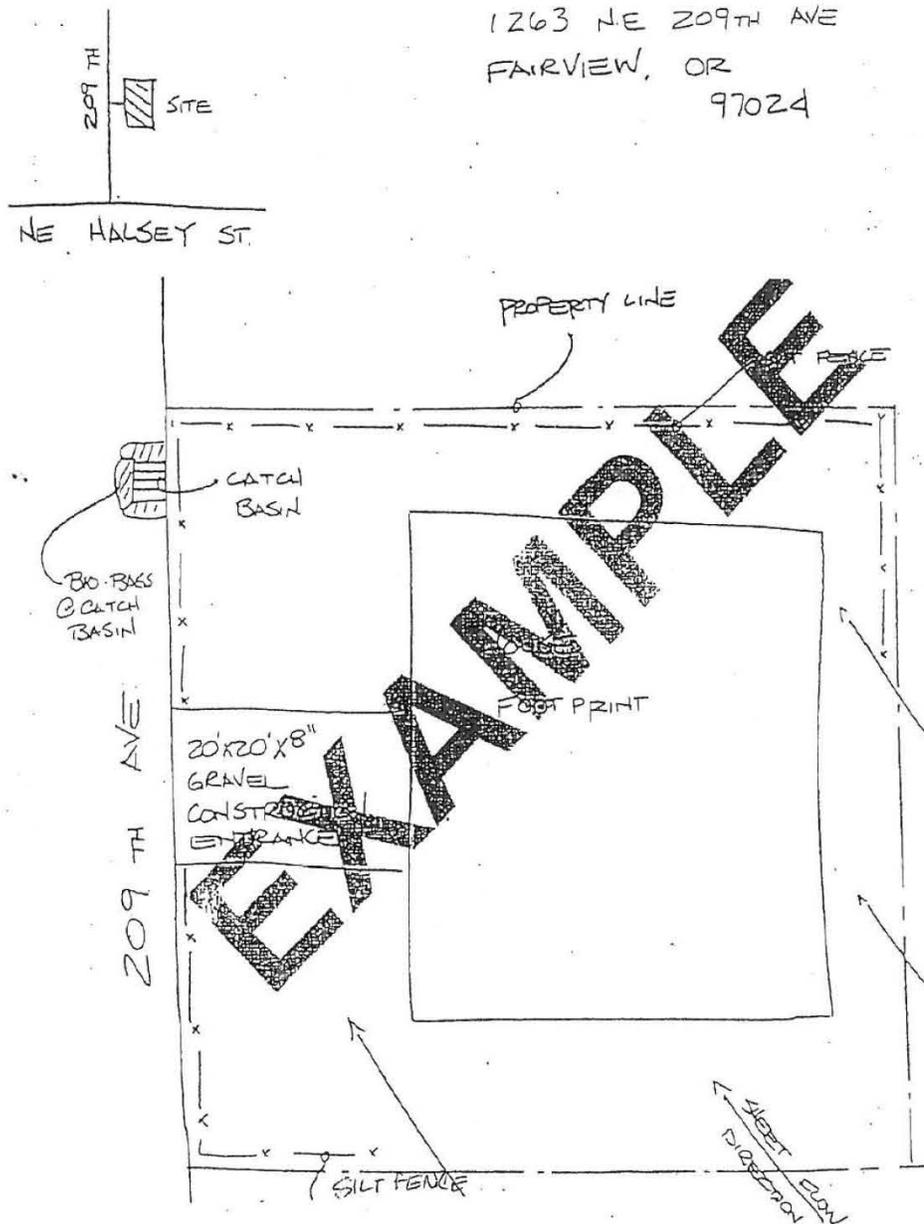

**SUMMARY OF EROSION CONTROL FEES
EROSION CONTROL PLANS AND INSPECTION FEES**

Plan Check Fee:

65 % of Erosion Control Inspection Fee (x .65)

Erosion Control Inspection Fees:

For A Building Permit Action

Building Value	Charges
Up to \$100,000	\$48 for Value Up to \$100,000
Over \$100,000	\$30 for Each Additional \$100,000 of Value or Fraction Thereof

For Developments Not Requiring A Building Permit

(grading, building streets and utilities in a Subdivision)

Value	Charges
Up to 1 Acre	\$120
Over 1 Acre	\$120 for First Acre
	(Plus \$30 for Each Additional Acre or Fraction Thereof)

FEE TOTALS

(To be completed by the City of Fairview)

Number of Acres Disturbed:		Acres: _____
Erosion Control Inspection Fee (up to one acre):		\$ <u>120.00</u>
Each Additional Acres or Fraction x \$30:		\$ _____
Subtotal Erosion Control Inspection Fee:		\$ _____
Plan Check Fee (65% of subtotal):	(x .65)	\$ _____
TOTAL EROSION CONTROL FEE:		\$ _____

**EROSION CONTROL MAINTENANCE PLAN
(All Construction)**

Maintenance measures required (check applicable measures):

 Gravel construction entrance.

Maintain a minimum of 8 inches of gravel.

 Temporary sedimentation fence or alternate measures.

Inspect daily and clean sediment build-up daily prolonged rainfall and after each storm.

 Excavated materials (protect from erosion).

Inspect silt fence or alternate erosion control device and remove sediment build-up.

 Excavated materials covered during wet weather season.

Inspect plastic cover, or alternate, on excavated materials (November 1 - April 30).

 Provide area for cement trucks to clean out their tanks.

Cleaning and washing out cement trucks in street areas, catch basins or drainage ways are not allowed.

EROSION/SEDIMENTATION CONTROL (ESC) MEASURES

**MINIMUM ESC REQUIREMENTS
DURING CONSTRUCTION:**

Sedimentation Facilities
Stabilized Construction Entrance
Perimeter Runoff Control
Clearing and Grading Restrictions
Cover Practices
Construction Sequence
Other _____

**MINIMUM ESC REQUIREMENTS
FOLLOWING CONSTRUCTION:**

Stabilize Exposed Surface
Remove and Restore Temporary ESC Facilities
Clean and Remove All Silt and Debris
Ensure Operation of Permanent Facilities
Other _____

The erosion control site plan must be prepared and submitted in accordance with the "Technical Guidance Handbook". Attach erosion control drawing (*see attached example*). Subdivision, commercial and industrial developments require a comprehensive erosion control plan.

I have read and will comply with the above, and will construct and maintain ESC measures, as necessary, to contain sediment on the construction site. I further certify that any and all work performed shall be in accordance with the ordinances of the City of Fairview and the laws of the State of Oregon pertaining to the work described herein, and if not in compliance, a STOP WORK ORDER will be issued.

OWNER SIGNATURE

APPLICANT SIGNATURE

DEPARTMENT APPROVAL – INITIAL & DATE
PUBLIC WORKS DEPT: _____

Erosion Control Permit Application
City of Fairview

1300 NE Village St., Fairview, Or 97024

Community Development – Permits Desk 503 674-6206

Inspection requests may be made by: Phone: 503 674-6244

Application No.:	Permit No.: EC
Date Received:	Expire date:
Date Issued:	Issued By:
Assoc. Permit No.:	Receipt No.:

General Contractor Name & Address:

Applicant Name & Address:

Excavation Contractor Name & Address:

Owner Name & Address:

CCB#: _____ **Exp. Date:** _____

Telephone Numbers

Applicant: _____
Owner: _____
General Contractor: _____
Excavation Contractor: _____
Site/Job: _____

Property Description/Address:

Subdivision Name: _____
Street Address & Cross Street/Located:

24 Hr/After-Hours Emergency Contact

Name: _____
Title: _____
Telephone: _____

Legal Description

Tax Lot No.: _____
1/4 Section: _____
Site Size, Acres: _____

Location/Address where spoils leaving site will be taken: (note: permits required)

Disturbed/Work Area, Acres: _____

Site runoff drains to: (circle one)

Catch-basin Ditch Pipe Creek

(circle one) Private Property
Public Right-Of-Way

EROSION CONTROL CONSTRUCTION SCHEDULE (All Construction)

Start Excavation:

Erosion control measures must be in place.

Date: _____

Construction completed, soil not stabilized:

Erosion control measures must remain in place.

Date: _____

Ground cover established:

Erosion control measures may be removed only after permanent site ground covers are in place.

Date: _____

Demolition work requires a separate demolition/abandonment permit.
